

 VGS2M JOINT VENTURE	Atlanta Airport Daily Report						
	Day	Thursday					
	Date	2/12/2026					
Management @ Site							
Name	Position	Phone	Email				
Jerald Mitchell	VGS2M General Manager	771-210-1255	gerald.mitchell@versar.com				
Cruz Santiago	VGS2M Compliance Manager	470-336-9922	Cruz.Santiago@versar.com				
Sammy Exantus	VGS2M Facility Manager	771-210-1452	sammy.exantus@versar.com				
Justin Deadwyler	VGS2M Program Manager	470-702-2109	justin@2mnext.com				
Nia Thomas	Corporate QHSE	240-252-2304	Nia.Thomas@versar.com				
Weather Conditions							
Hours Onsite							
VGS2M Resources		Contractor					
Name	Hrs. On site	Company Name	Resource Name	Hrs. On site			
Cruz Santiago	8	Environmental Restoration	OSRO	8			
Jerald Mitchell	8	BASHA Services, LLC	OSRO	8			
Nia Thomas	0						
Sammy Exantus	8						
Justin Deadwyler	8						
Total Hrs.	32		Total Hrs.	16			
Daily Summary 1. Focus on AATC, corralling debris and creating strategic booms in preparation for the rain. The crew went out in the morning and checked all collection areas. Changed booms as needed and removed oil with pads and pool skimmers. 2. Waste disposal has been organized and will empty one 20-yard bin tomorrow. The total waste is >3, 20-yard bins. 3. Lab results with MDLs and J scores arrived today and are attached for a more specific analysis.							
Fuel Collection: The tanks were not completely full and have not yet been emptied. Currently in tank two (approx.): 985 gal. fuel, 3402 gal. water. Tank three: 562 gal. fuel, 2059 gal. water. Tank one: empty. Total Volume of Fuel Collected: NOTE: these are approximate figures and are subject to change. Total fuel volume was determined using manual tank gauging in the field with fuel-finding paste when the tanks are full. The frac tanks are positioned on an approximate one-foot incline, which may distort the calculated total volume. More accurate figures will be determined at the point of disposal.							
Fuel Recovered							
Date	Volume	Date	Volume	Date	Volume	Date	Volume
2-Feb	2520	8-Feb	Tanks not full	14-Feb		20-Feb	
3-Feb	3608	9-Feb	5270	15-Feb		21-Feb	
4-Feb	2452	10-Feb	1330	16-Feb		22-Feb	
5-Feb	Tanks not full	11-Feb	Tanks not full	17-Feb		23-Feb	
6-Feb		12-Feb		18-Feb		24-Feb	
7-Feb		13-Feb		19-Feb		25-Feb	
						Total	15180
PCW Volume							
Date	Volume	Date	Volume	Date	Volume	Date	Volume
2-Feb	11760	8-Feb	Tanks not full	14-Feb		20-Feb	
3-Feb	8525	9-Feb	21508	15-Feb		21-Feb	
4-Feb	7104	10-Feb	9230	16-Feb		22-Feb	
5-Feb	Tanks not full	11-Feb	Tanks not full	17-Feb		23-Feb	
6-Feb		12-Feb		18-Feb		24-Feb	
7-Feb		13-Feb		19-Feb		25-Feb	
						Total	58127



VGS2M JOINT VENTURE

Atlanta Airport Daily Report Outfall FR-1/AATC (Site 2)

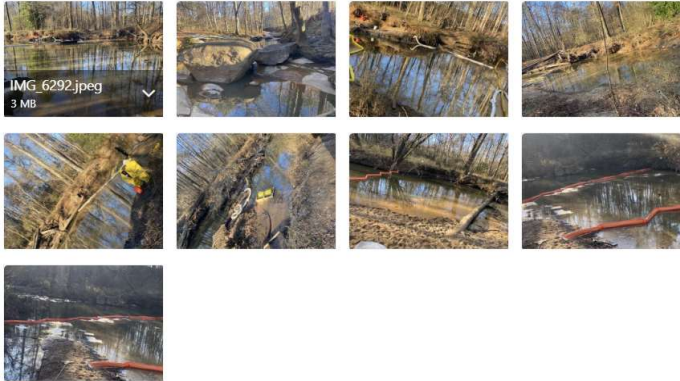
Day Thursday
Date 2/12/2026

Activity Log

Planned Daily Activities Description

Still collecting product off the water. Repositioning and replacing booms as needed.

Activity	Comments
A - Containment booms deployed and checked (provide status)	Replacing as needed
B - Vac truck recovery operations scheduled or underway	3
C - Water Samples scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	Basha is using skimmers
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	60%-70%
G - Sheen visibility approx. area	500-1000 sq. ft.

Start of Day Photos	
---------------------	---

End of Day Photos	
-------------------	--

Photos	Comments
New or Continued Issues Encountered	



VGS2M JOINT VENTURE

Atlanta Airport Daily Report Forest Parkway (Site 3)

Day	Thursday
Date	2/12/2026

Activity Log

Planned Daily Activities Description

Collecting and maintaining. Visited the site twice.

Activity	Comments
A - Containment booms deployed and checked (provide status)	Maintained - will be replaced tomorrow
B - Vac truck recovery operations scheduled or underway	n/a
C - Water Samples non-scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	n/a
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	~80%
G - Sheen visibility approx. area	50 sq. ft.

Start of Day Photos



End of Day Photos



Photos

Comments

New or Continued Issues Encountered



Atlanta Airport Daily Report Lee's Mill Rd (Site 4)

Day Thursday
Date 2/12/2026

Activity Log

Planned Daily Activities Description

Maintaining and collecting. One boom was repositioned after migrating downstream.

Activity	Comments
A - Containment booms deployed and checked (provide status)	1 boom replaced
B - Vac truck recovery operations scheduled or underway	n/a
C - Water Samples non-scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	n/a
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	Almost complete. Maintenance work with top scum that migrates overnight.
G - Sheen visibility approx. area	50 sq. ft.

Start of Day Photos	
---------------------	--

End of Day Photos	
-------------------	--

Photos	Comments



Atlanta Airport Daily Report Upper Riverdale Rd (Site 5)

Day Thursday
Date 2/12/2026

Activity Log

Planned Daily Activities Description

Absorbent oil-dry was added to the roll-off bin as the waste management team can't take liquid waste.

Activity	Comments
A - Containment booms deployed and checked (provide status)	maintained - will be exchanged tomorrow
B - Vac truck recovery operations scheduled or underway	n/a
C - Water Samples non-scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	n/a
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	Progressing
G - Sheen visibility approx. area	200-500 sq. ft.

Start of Day Photos

End of Day Photos

Photos	Comments
	Site is only accessible via boat



Atlanta Airport Daily Report Valley Hill Rd (Site 6)

Day Thursday
Date 2/12/2026

Activity Log

Planned Daily Activities Description

Residual was skimmed from the surface.

Activity	Comments
A - Containment booms deployed and checked (provide status)	Maintained
B - Vac truck recovery operations scheduled or underway	n/a
C - Water Samples non-scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	n/a
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	80%
G - Sheen visibility approx. area	<25sqft

Start of Day Photos



End of Day Photos



Photos

Comments

New or Continued Issues Encountered



Atlanta Airport Daily Report Rock Quarry (Site 1)

VGS2M JOINT VENTURE

Day	Thursday
Date	2/12/2026

Activity Log

Planned Daily Activities Description

n/a

Activity	Comments
A - Containment booms deployed and checked (provide status)	n/a
B - Vac truck recovery operations scheduled or underway	n/a
C - Water Samples non-scheduled or to be taken	Monday, February 16th
D - Skimmers being utilized	n/a
E - Water Samples status with lab (sent/scheduled return, etc.)	Returned
F - Percentage of collection	Near total
G - Sheen visibility approx. area	None

Start of Day Photos



End of Day Photos

Photos

Comments

New or Continued Issues Encountered
